

BRUHAT BANGALORE MAHANAGARA PALIKE

WELCOME TO RI-MAHADEVAPURA DIVISION


Details of ORR Connecting Road Pertains to RI-Mahadevapura BBMP

SI No	Road Name	Length in Km	From	То
1	Sarjapura Road	5.00	Iblur	Carmelaram Junction
2	Ambalipura Bellandur Road	1.30	ORR	Sarjapura Road
3	Haraluru Road	3.25	Sarjapura Road	Kudlu Junction
4	Kasavanahalli Road	2.50	Sarjapura Road	Choodsandra
5	Gear School Road	4.00	ORR	Sarjapura Road
6	Panathur Balagere Road	6.00	ORR	Varthur Gunjur Road
7	New Horizon College Road	0.70	ORR (Wells Fargo)	Gear School Road
8	Choulkere Road	2.90	ORR (Devarabeesanahalli)	AET Junction (Gear School Road)
9	Devarabeesanahalli Road	1.30	ORR (Devarabeesanahalli)	Gear School Road
10	Kariyammana Agrahara Road	1.80	ORR (Kadubeesanahalli)	ORR (Sakra Hosp)
11	Sakra Hospital Road	1.00	ORR (Devarabeesanahalli)	Bellandur Kodi
12	Bellandur Main Road via Yamalur	4.50	ORR bellanduru	OAR Yamalur Signal

SI No	Road Name	Length in Km	From	То
13	Kempapura Main Road	5.40	Yamalur Kodi	OAR Wind Tunnel Junction
14	Croma Road	1.80	ORR (Croma)	Balagere Road
15	Gunjur Palya Road	3.10	Panathur Balagere Road	Carmelaram Road
16	Carmelaram Road	4.50	Sarjapura Road	Gujur SH35
17	Old Airport Road	8.6	Surajandas Junction	Varthur Kodi
18	Varthur Gunjur Road (SH-35)	4.7	Varthur Kodi	Gunjur
19	Doddanekundi Main Road	2.4	ORR (ISRO Junction)	OAR
20	Doddanekundi village Road	1.30	ORR (Doddanekundi)	Doddanekundi Road
21	Graphite India Road	4.80	OAR Kundalahalli	Whitefield Road
22	Alphine Echo Road	2.30	ORR Rain Bow hospital	Graphite India Road

Road Name:		Sarjapura Road			
From	ORR Iblur Junction	То	Carmelaram		
Length	5.00 Km	Width	10.5 Mtrs Wide, 2 Carriage Way		
Importance		This road is useful for Traffic flow from Electronic city to Whitefield and Varthur Road by avoiding ORR.			
Present St	Present Status		➤ Main Carriage way Work Completed and is in Good Condition		
Key Issues		 ➤ Land Acquisition in process for service Roads ➤ Underpass work to be started ➤ Gail Gas pipeline work proposed by Gail India 			

Sarjapur Road from Iblur Junction to Carmelaram Road

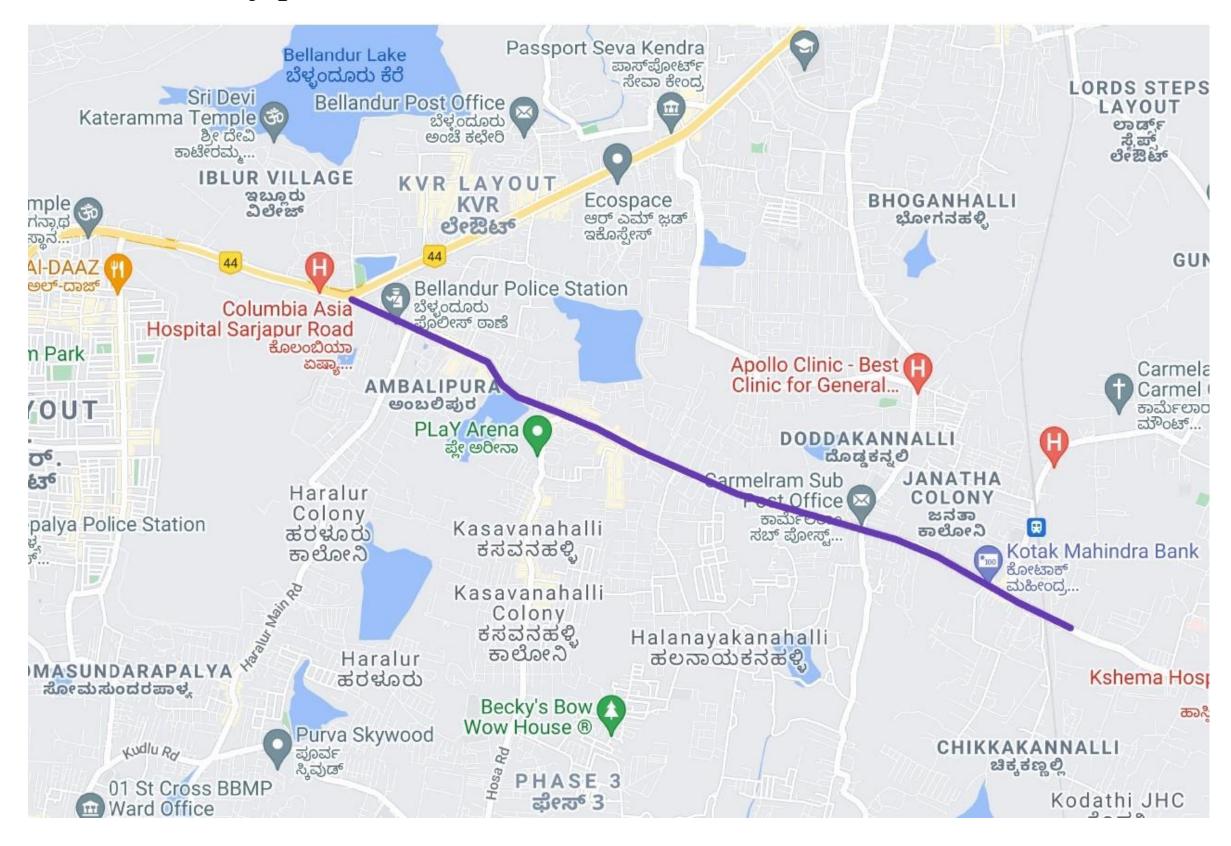











Road Name:		Ambali	Ambalipura Bellandur Road,		
From	ORR Bellandur	То	Sarjapura Road		
Length	1.30 Km	Width	12 to 15 Mtrs		
Importance		Belland	This road is useful for Traffic flow from Bellandur to Sarjapura Road by avoiding ORR from Bellandur to Iblur Jn.		
Present S	Present Status		> Road work under progress.		
On Going Works		 ➤ Drain and Footpath Work under progress ➤ 1.10 Km Drain and Footpath work completed on either side of the Road. 			
Key Issues			➤ BESCOM UG Cable work under progress ➤ Gail Gas pipeline work proposed by Gail India		

Ambalipura Bellandur Road from ORR Bellandur to Sarjapura Road

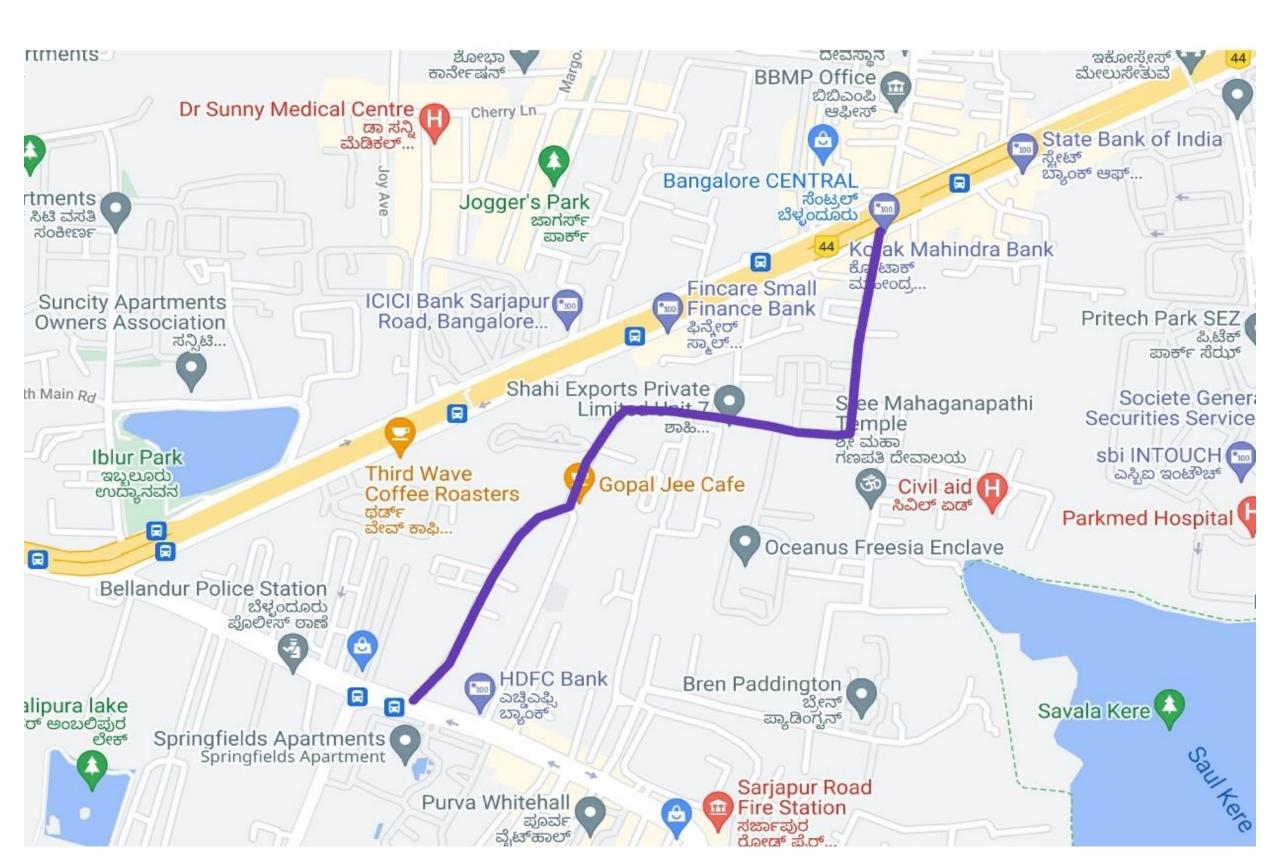






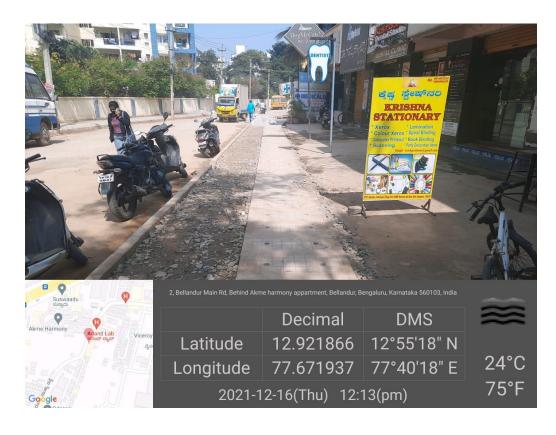





Road Name:		Bellandur Main Road via Yamalur		
From	ORR Bellandur	То	OAR Yamalur Signal	
Length	4.50Km	Width	12 to 15Mtrs	
Importance		This road is useful for Traffic flow from Bellandur to OAR by avaoiding traffic from ORR Bellandur to Marathahalli.		
Present Status		 Road is Asphalted upto Yamalur Kodi (From Ch:0.00Km to 3.00Km) and is in Good Condition. From Yamalur Kodi to Yamalur Signal road (From Ch: 3.00Km to 4.50Km) is Dug for Laying UGD Line by BWSSB, Presently BESCOM UG Work under progress. 		
On Going Works		Tender is Invited for restoration of UGD Road cut Portion.		
Key Issues		> BWS	COM UG Cable work under progress. SB UGD Work to be started from ORR or to Bellandur Kodi	

Bellandur Main Road from ORR Bellandur to OAR Yamalur Signal

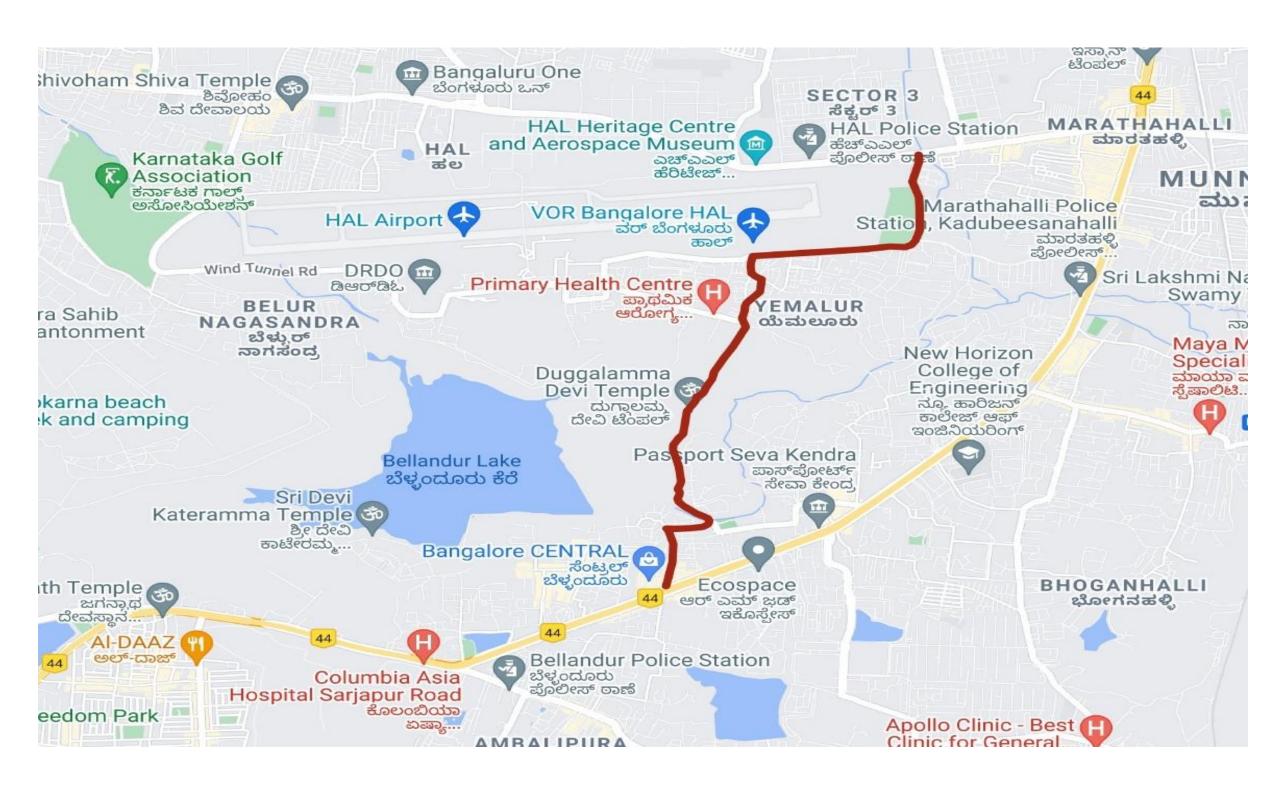



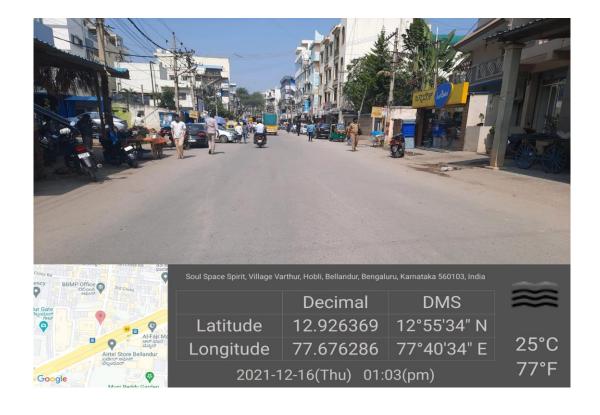


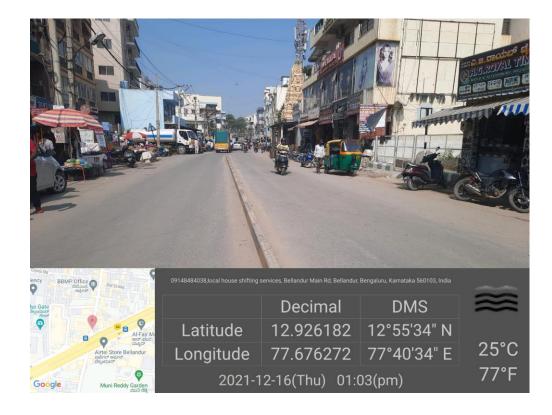



Road Name:		Kempapura Main Road		
From	Yamalur Kodi	То	OAR Wind Tunnel Junction	
Length	5.40Km	Width	12Mtrs	
Importance		This road is useful for Traffic flow from Bellandur to OAR by avoiding traffic from ORR Bellandur to Marathahalli and also OAR at HAL.		
Present Status		From Kempapura Wind Tunnel Road to Challagatta (SWD)(Ch:1.20Km to Ch:4.50km) Asphalt work completed on 14-12-202.		
On Going Works		 ➤ Drain Work under progress from Yamalur Kodi to Kempapura (Ch:0.00 to Ch:1000.00m). ➤ Restoration of BWSSB UGD Road Cut started. 		
Key Issues		> BESCOM UG Cable work under progress		

Kempapura Main Road from Yamalur Kodi to OAR Wind Tunnel Junction

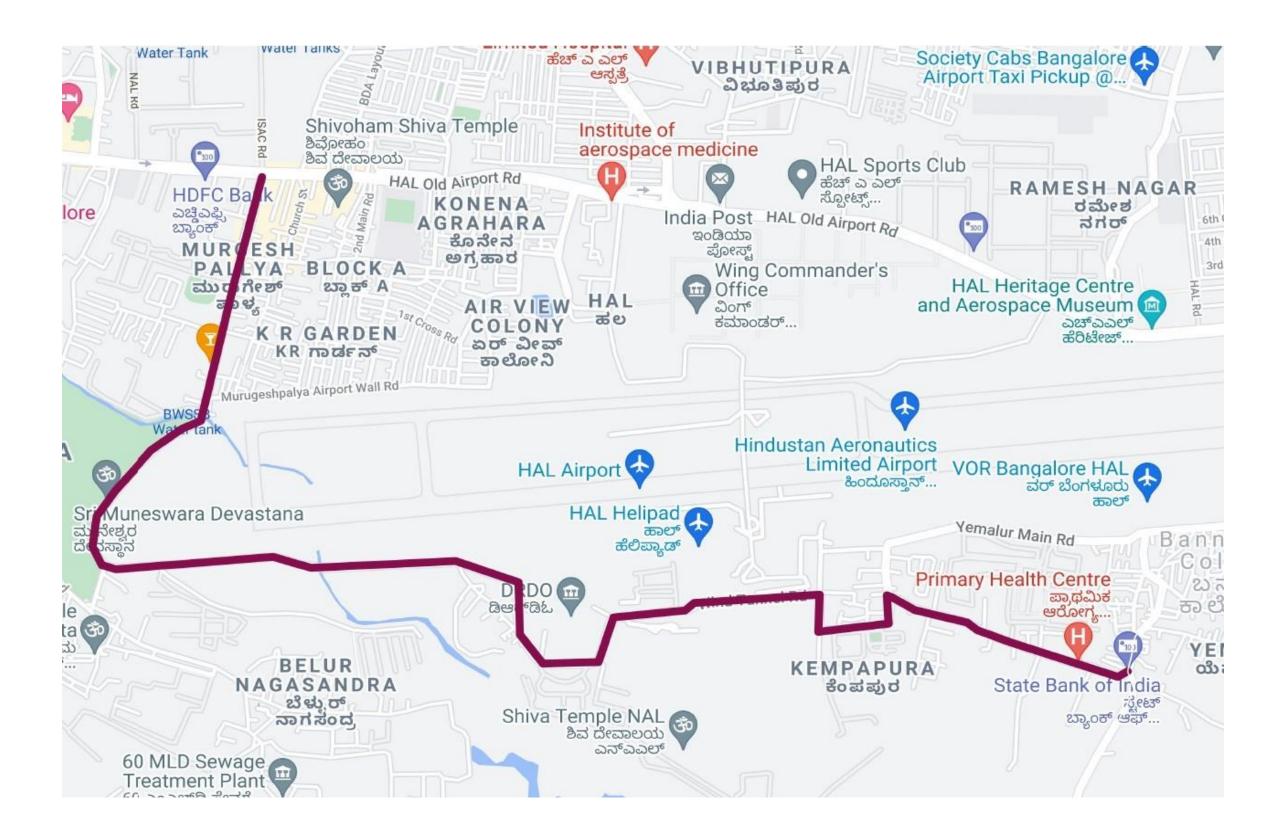

Work Photos (Ch:1.20Km to Ch:4.50Km Drain work in progress









Work Photos (Ch:0.00m to Ch:1000.00m Drain work in progress)










Road Name:		Kariyammana Agrahara Road	
From	ORR (Kadubeesanhalli)	То	ORR (Sakra Hosp Road) via Kariyammana Agrahara Village
Length	1.80Km	Width	10 to 15Mtrs
Importance		This road is useful for Traffic flow from ORR (Kadubeesanhalli) to Sakra Hosp Road. The reach from Kariyammana Agrahara Burial Ground to sakra Hosp is ward road	
Present Status		and	d Cut for BWSSB UGD Work is Restored Road is Asphalted on 12-12-2021 (From 0.00Km to 0.5Km)
On Going Works		(From € Road 18.00m	Work and Footpath Work is in progress Ch:0.00Km to 0.5Km) is Proposed for widening for a width of trs from ORR(Kadubeesanhalli) to Yamalur and Land Acquisition in process.

Kariyammana Agrahara Road from ORR (Kadubeesanhalli) to ORR (Sakra Hosp Road) via Kariyammana Agrahara Village

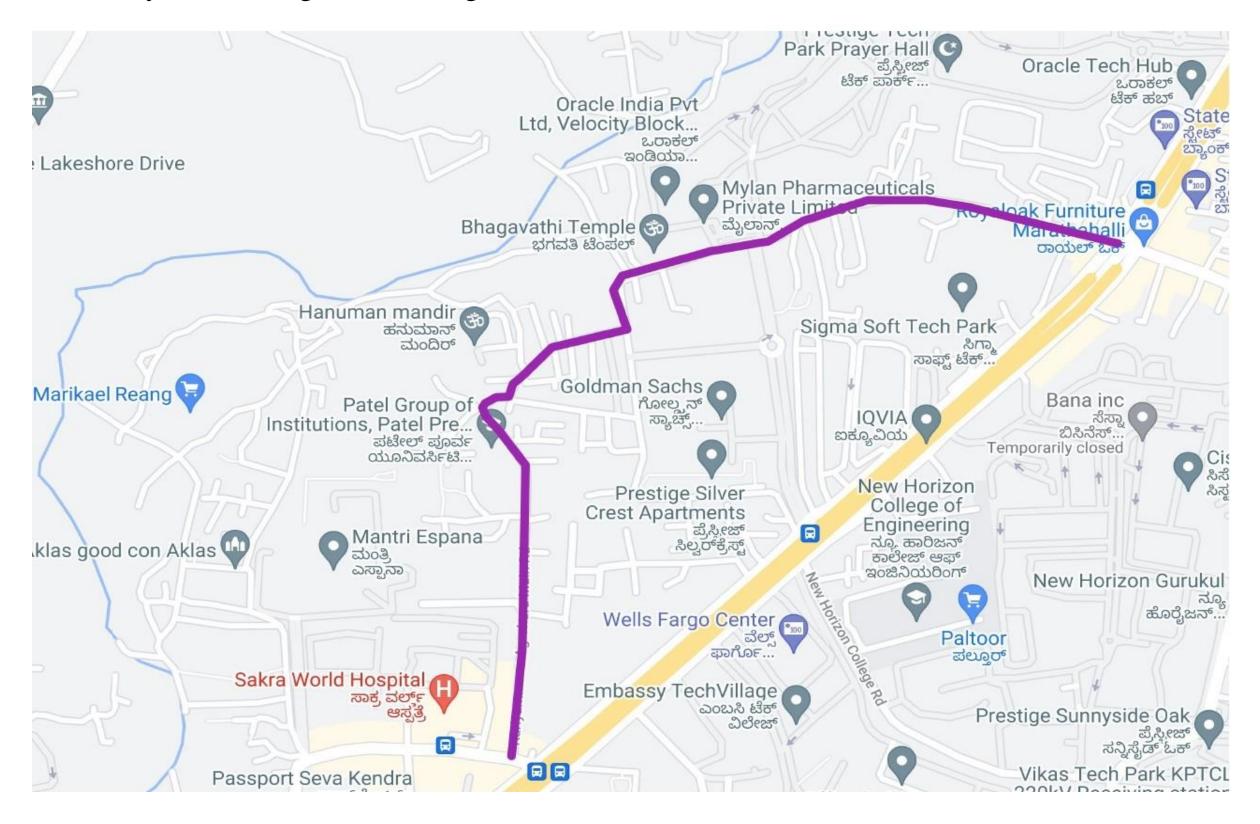











Road Name:		Haralur	Haraluru Road		
From	Sarjapura Road	То	Kudlu Junction		
Length	3.25Km	Width	12 to 15 Mtrs		
Importance		Electron	This road is useful for Traffic flow from Electronic city to Whitefield and Varthur Road by avoiding ORR.		
Present S	Present Status		Main Road is Asphalted and is in Good Condition		
On Going Works		24.00M Constru	➤ Road Widening Work is proposed for 24.00Mtrs is to be started which includes Construction of Drain & Footpath and Land Acquisition under progress		
Key Issues		> BWS	 Land Acquisition and TDR Issues BWSSB UGD work to be taken up BESCOM UG Cable Work to be taken up 		

Haraluru Road from Sarjapura Road to Kudlu Junction Road

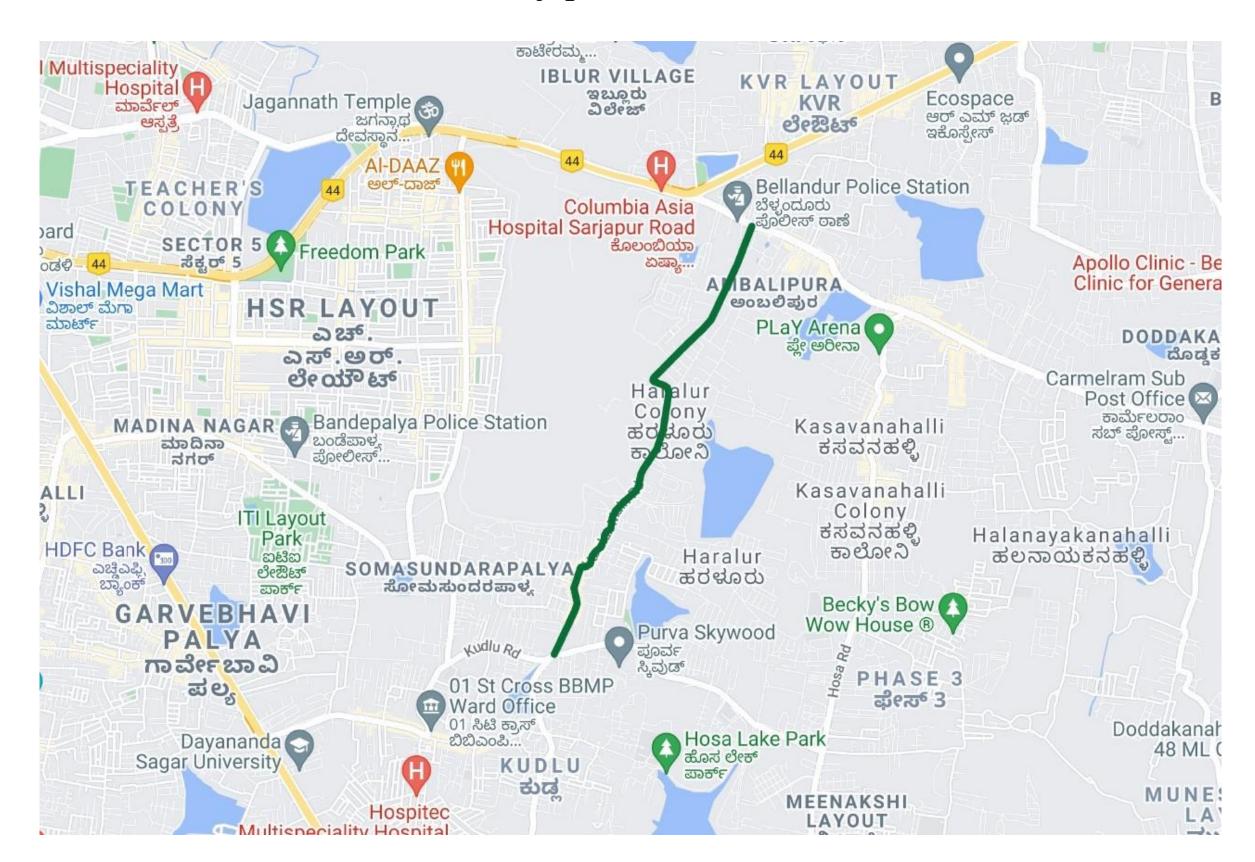

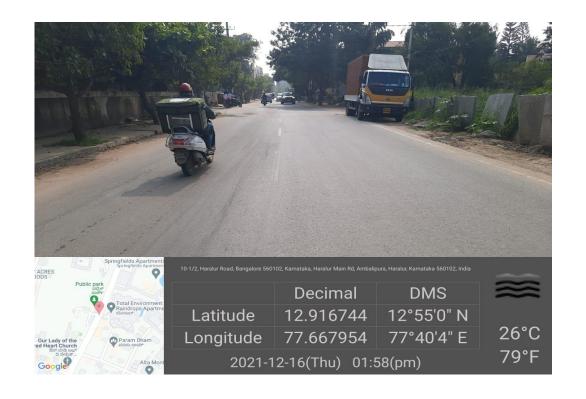










Road Name:		Kasavan	Kasavanahalli Road		
From	Sarjapura Road	То	Choodsandra Road		
Length	2.50Km	Width	12 to 15Mtrs		
Importance		This road is useful for Traffic flow from Electronic city to Whitefield and Varthur Road by avoiding ORR.			
Present S	Present Status		Main Road is Asphalted, Currently BESCOM UG Work under progress.		
On Going Works		➤ Road Widening Work is proposed for 18.00Mtrs and work started which includes Construction of Drain & Footpath and Land Acquisition under progress			
Key Issues			 Land Acquisition and TDR Issues BESCOM UG Cable work under progress 		

Kasavanahalli Road from Sarjapura Road to Choodsandra Road

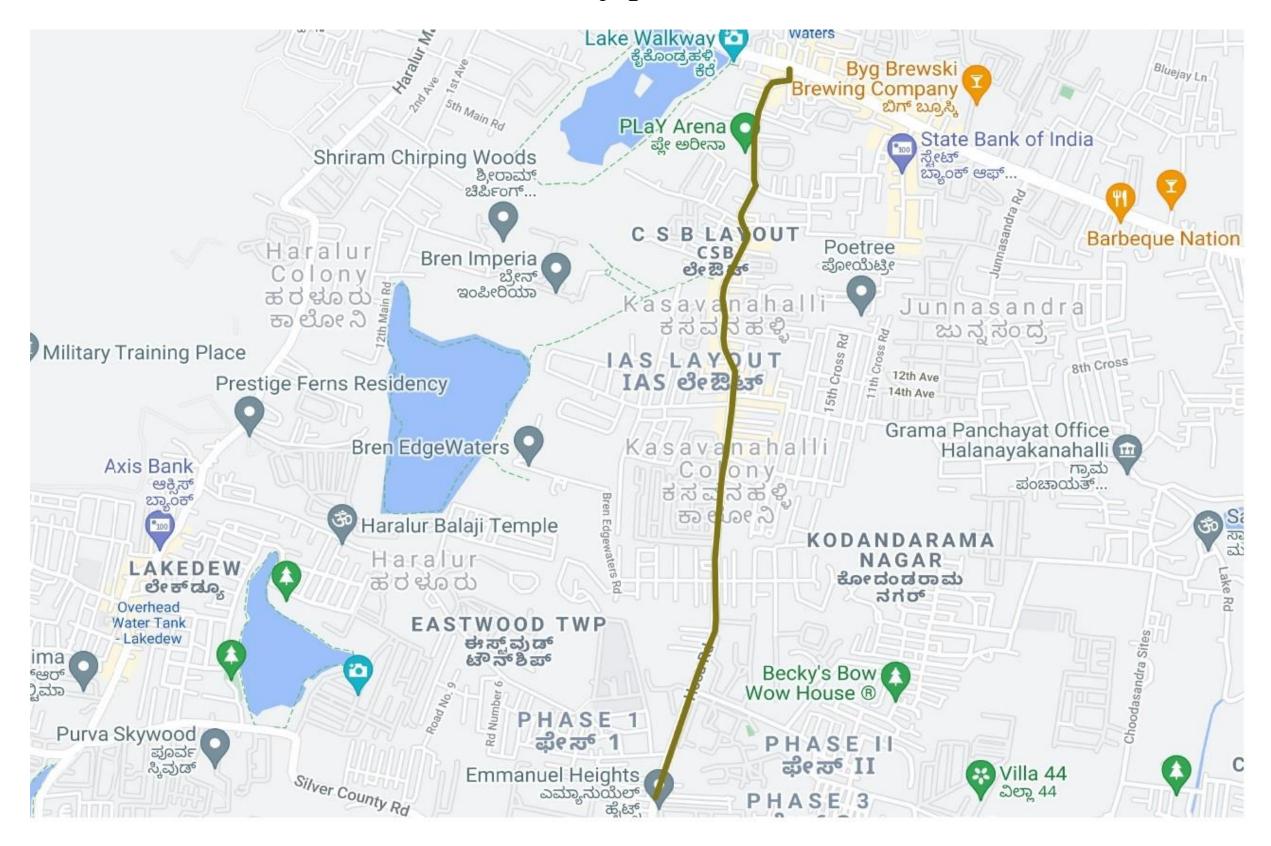

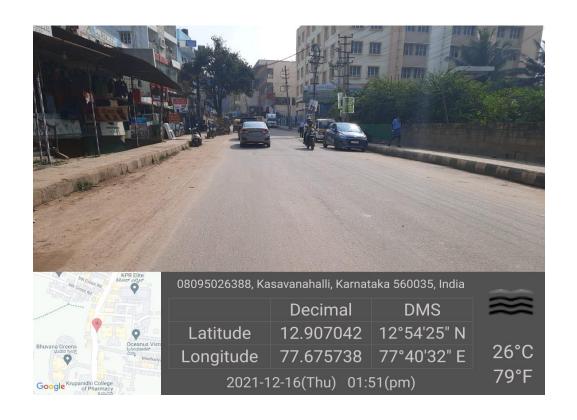

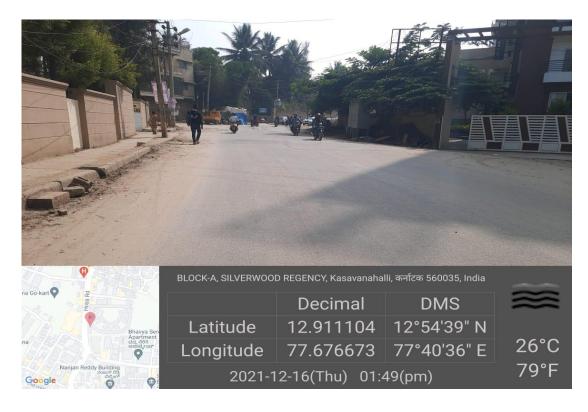






Road Name:		Gear School Road		
From	ORR	То	Sarjapura Road	
Length	4.00Km	Width	12 to 18 Mtrs	
Importance		This road is useful for Traffic flow from Sarjapura Road to ORR (Kadubeesanahalli)Road by avoiding ORR from Iblur to Kadubeesanahalli.		
Present Status		 Presently KPTCL and BESCOM Work is under progress. Water Leakages at few Locations and restoration work is under progress by BWSSB 		
On Going Works		 ➤ Drain and Footpath Work Completed. ➤ Balance Asphalt work will be started once other agencies complete the work. 		
Key Issues		➢ BESCOM UG Cable work under progress.➢ Road Dug up for BWSSB Water Leakage.		

Gear School Road from ORR to Sarjapura Road

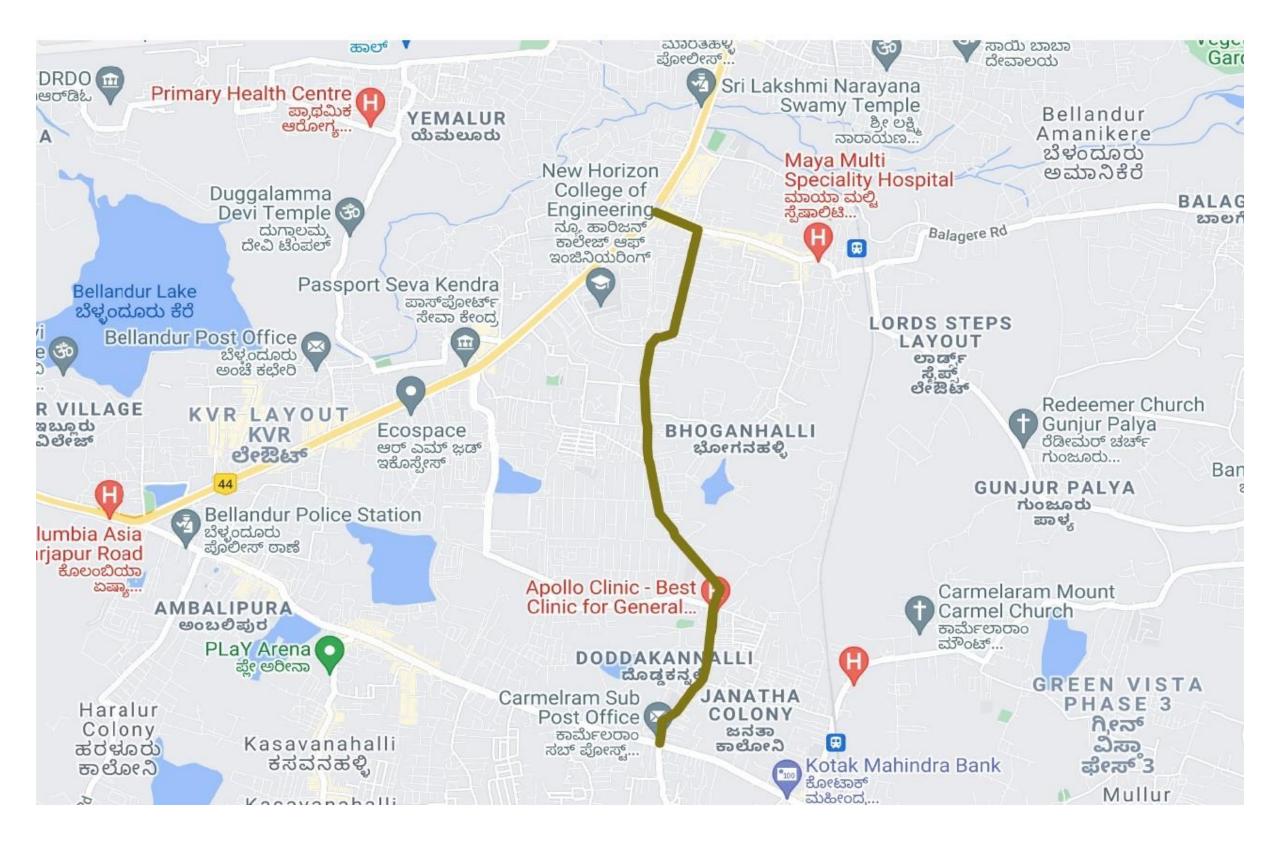









Road Name:		Panathu	Panathur Balagere Road		
From	ORR	То	Varthur Gunjur Road		
Length	6.00Km	Width	7Mtrs		
Importance		Kadube Road by	This road is useful for Traffic flow from Kadubeesanahalli ORR to Varthur Gunjur Main Road by avoiding ORR from Kadubeesanahalli to Marathahalli.		
Present Status			> 3.30Km of Road is Asphalted remaining length is motorable		
On Going Works			➤ Widening Work Under Progress➤ Drain Work under progress		
Key Issues		>BWS: >Tree (>Electrical Panation	COM UG Cable work under progress SB Work under Progress Cutting Issue rical Pole Shifting to be done hur & Varthur Village Limit Width of the to 9Mtrs.		











Panathur Balagere Road from ORR to Varthur Gunjur Road

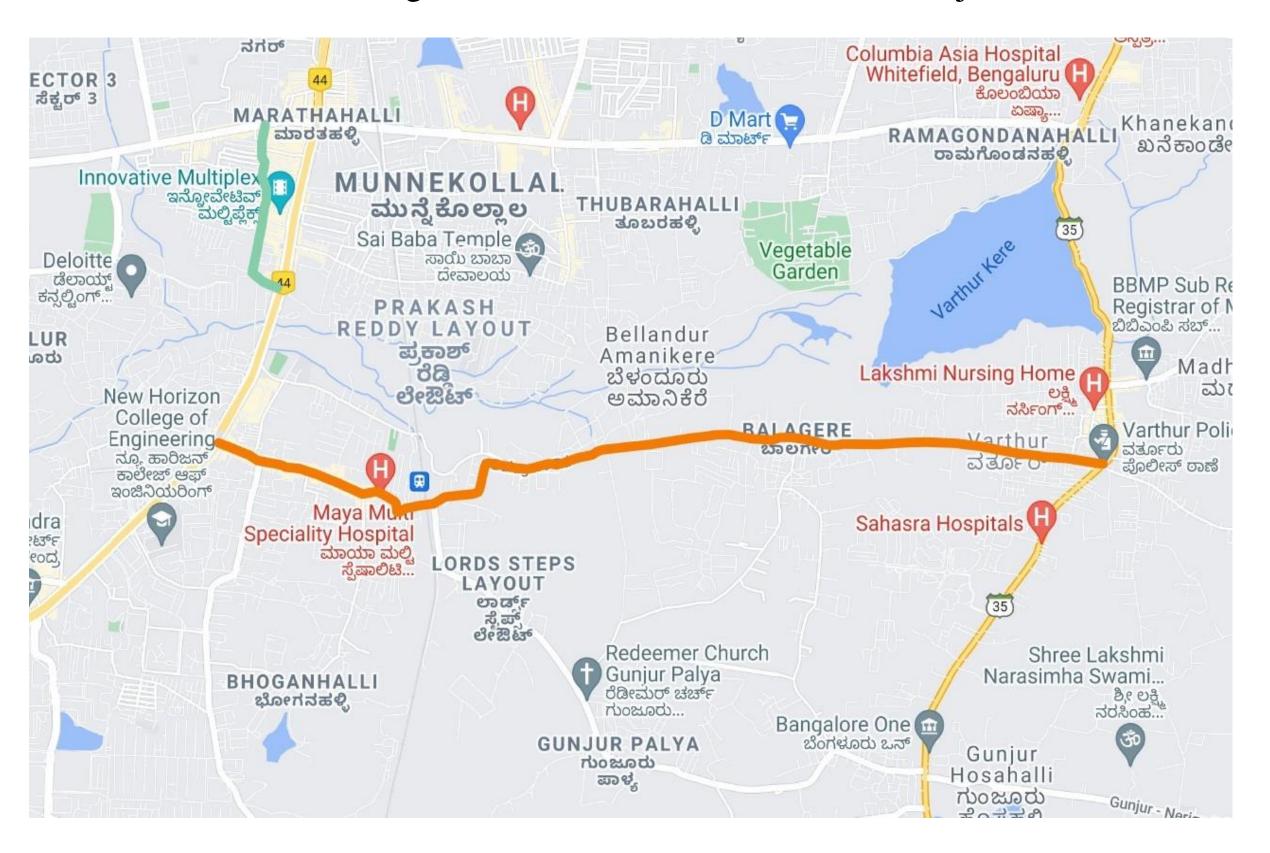


Road Name:		New Horizon College Road			
From	ORR(Wells Fargo)	То	Gear School Road		
Length	0.70Km	Width	15 to 24Mtrs		
Importance			This road is useful for Traffic flow from ORR to Gear School.		
Present S	Present Status		Road is in Good Condition		
On Going	On Going Works		 ➤ From Gear School Road this road Connects Gunjur. ➤ New Formation of 45Mtr Wide Road work is in progress. 		
Key Issues		 ➤ Land Acquisition and TDR Issues. ➤ Acquisition of Forest Land in Sy No 52 & 53 ➤ Electrical Sub Station Shifting ➤ Electrical Crematorium Shifting. 			

New Horizon College Road From ORR to Gear School Road

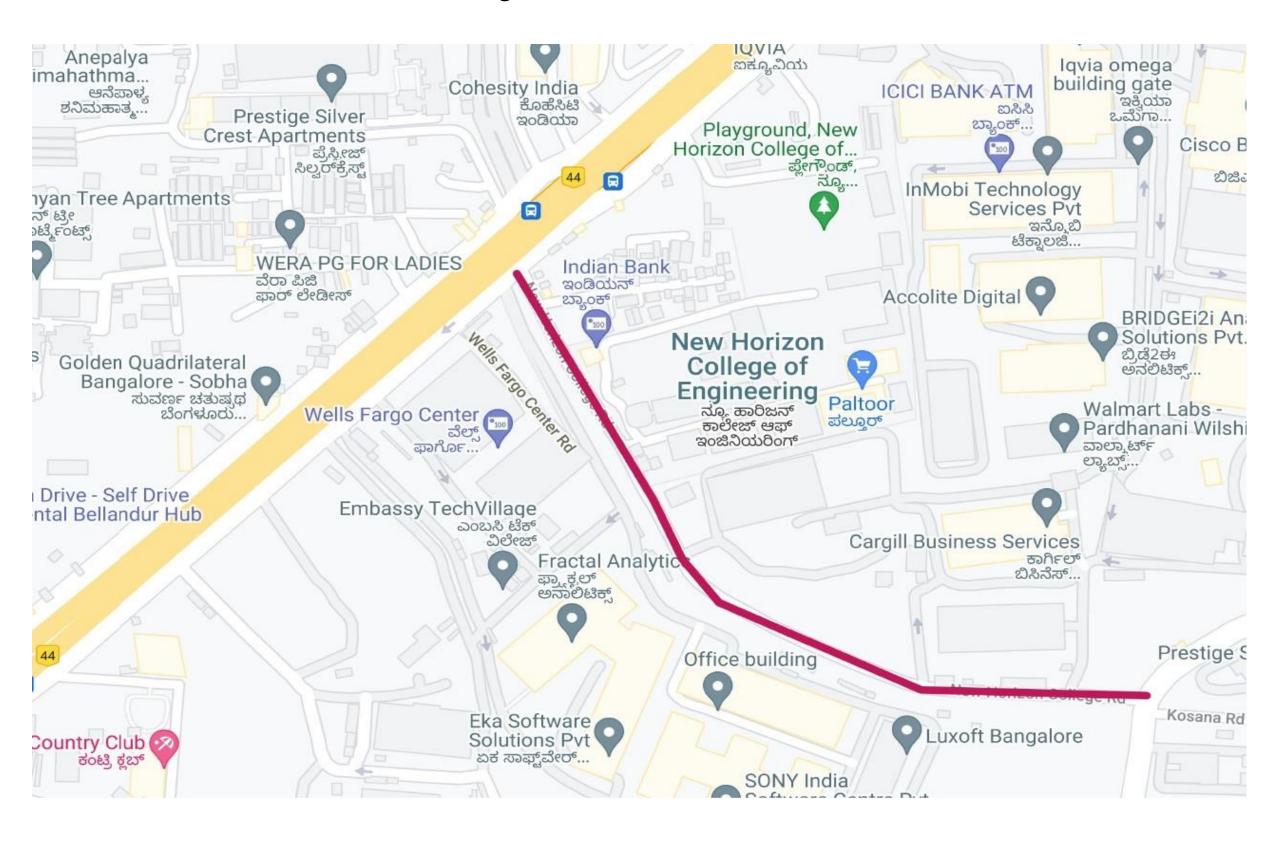



New Horizon College Road



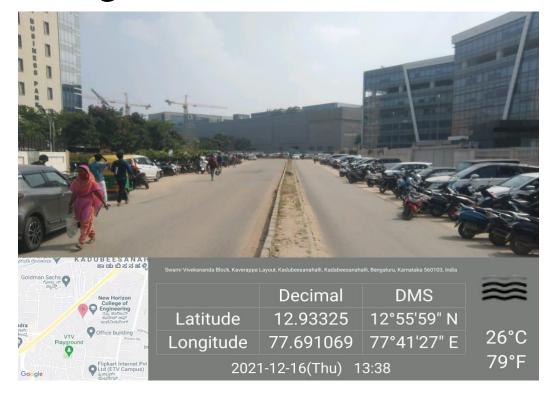


On Going Work - 45Mtrs Wide Road

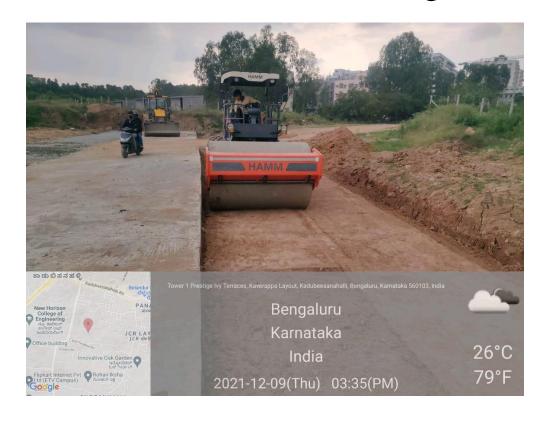


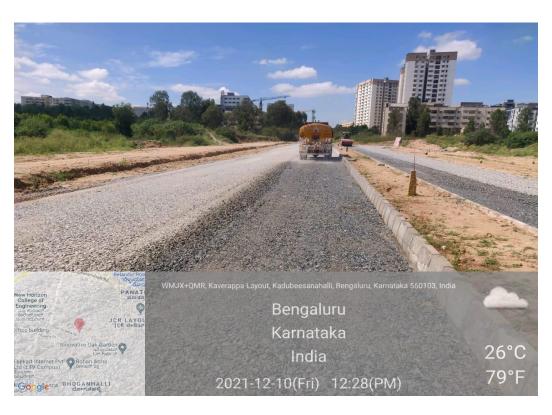


Road Name:		Choulkere Road	
From	ORR (Devarabeesa nahalli)	То	AET Junction (Gear School Road)
Length	2.90Km	Width	12 to 15Mtrs
Importance		This road is useful for Traffic flow from ORR (Devarabeesanahalli) to AET Junction (Gear School Road).	
Present Status		 BWSSB UGD Road cut Restoration work under progress BESCOM UG Cable work under progress 	
On Going Works		➤ Road Formation Work is in progress. ➤ LHS Drain and Footpath Work is in progress.	
Key Issues		➤ BESCOM UG Cable work under progress. ➤ Land Acquisition and TDR Issues at Road Widening portion.	

Choulkere Road from ORR (Devarabeesanahalli) to AET Junction (Gear School Road)

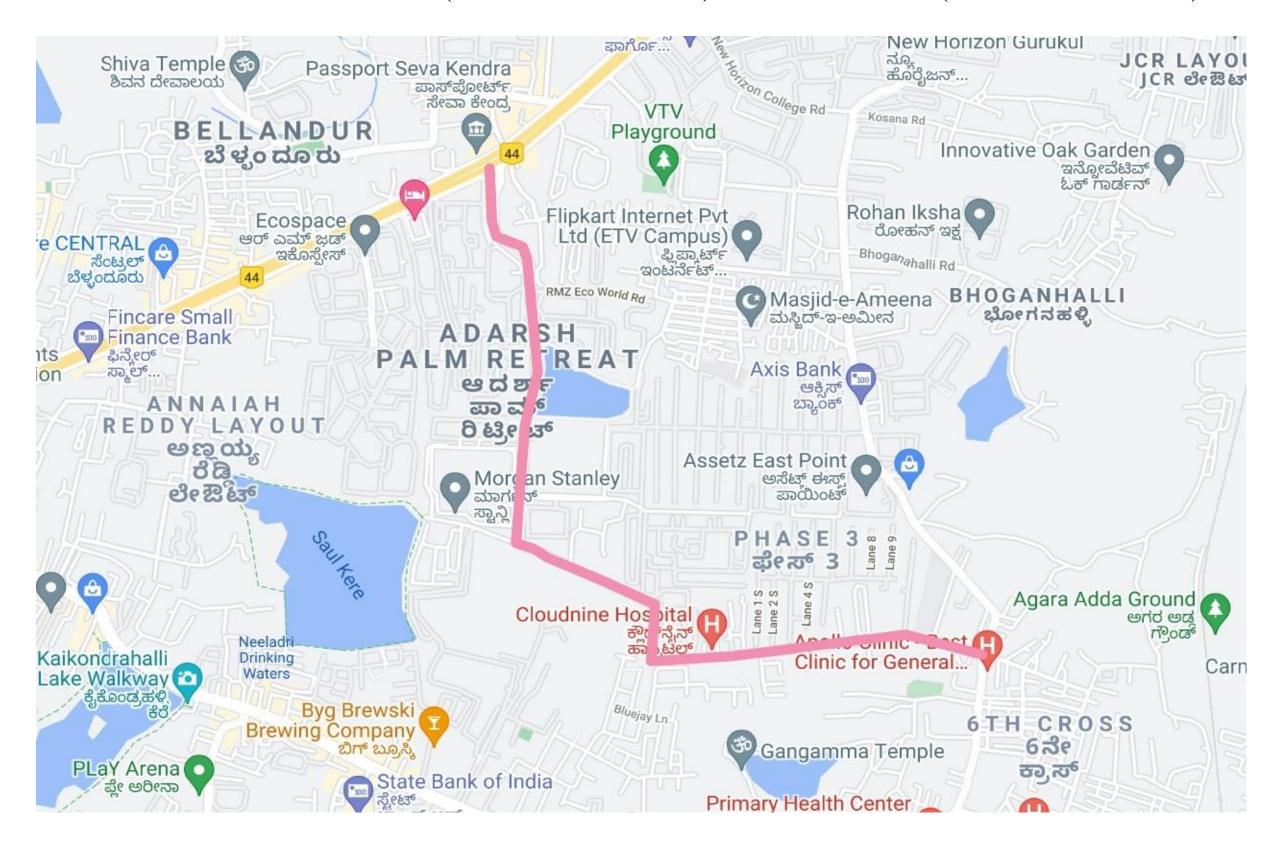

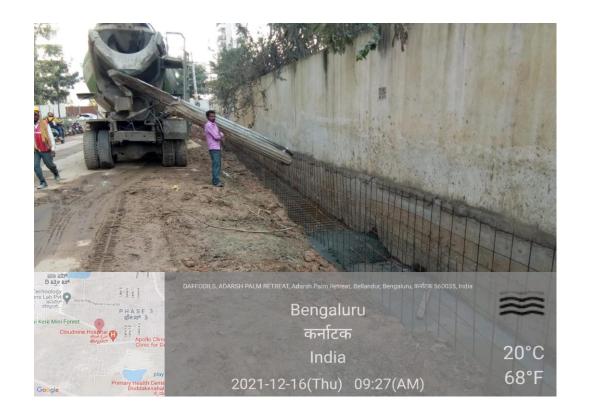

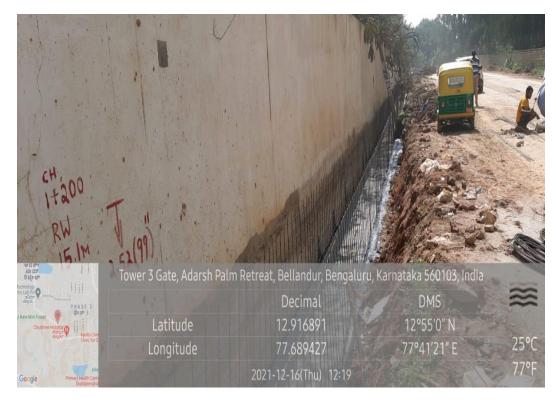






Road Name:		Devarabeesnahalli Road		
From	ORR (Devabeesna halli)	То	Gear School Road	
Length	1.30Km	Width	10 to 12Mtrs	
Importance		This road is useful for Traffic flow from ORR (Devarabeesanahalli) to Gear School Road.		
Present Status		> Drain	n work and Footpath Work Completed	
On Going Works		➤ Water leakages at few locations and Restoration work under progress by BWSSB ➤ Asphalt work will be taken up once water leakages are Restored.		

Devarabeesnahalli Road from ORR (Devarabeesanahalli) to Gear School Road

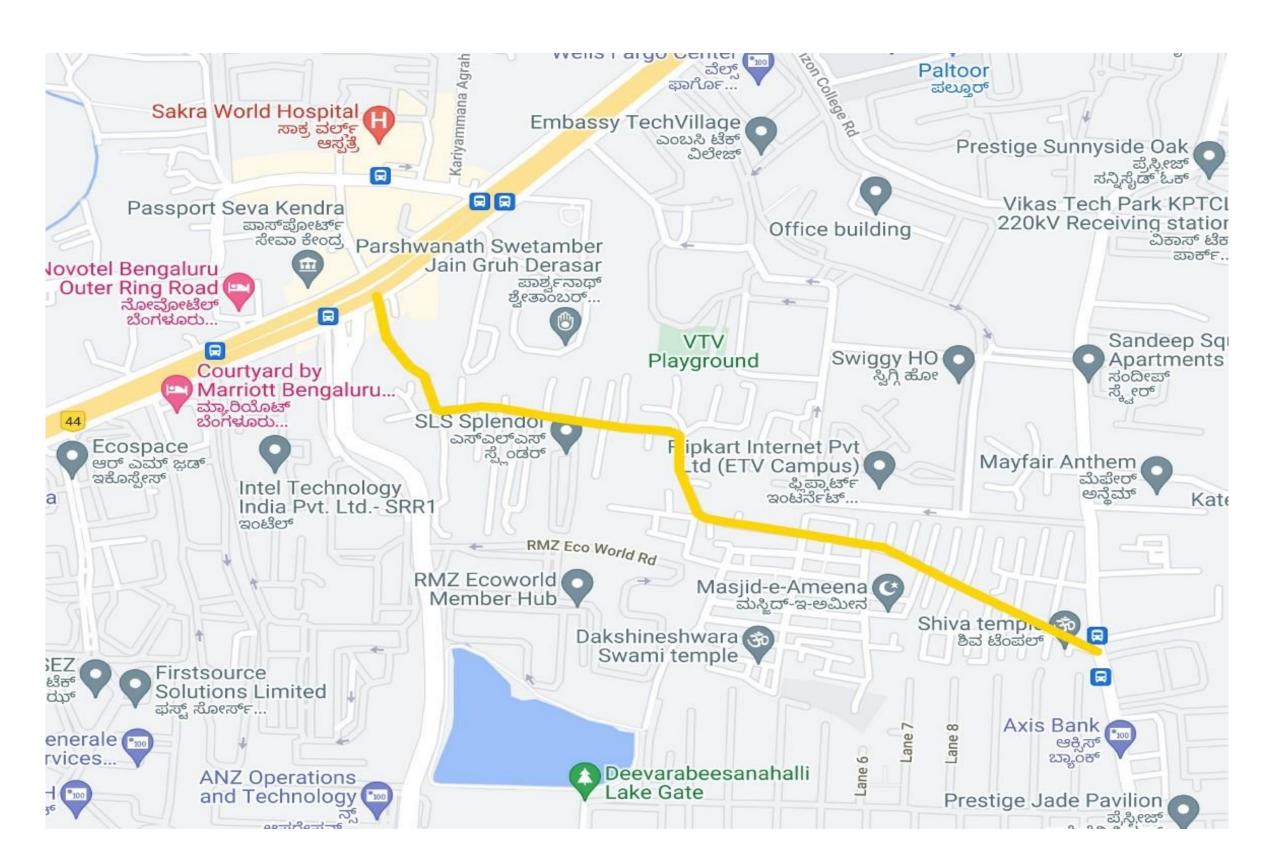











Road Name:		Sakra Hospital Road		
From	ORR (Devabeesnahalli)	То	Bellandur Kodi Road	
Length	1.00Km	Width	12 to 15Mtrs	
Importance		This road is useful for Traffic flow from ORR (Devabeesnahalli) to Bellandur Kodi Road by avaoiding traffic from Bellandur to ORR (Devabeesnahalli)		
Present Status		> Road	is Asphalted and in Good Condition.	
Key Issues		> BWS	COM UG Cable work to be started SB UGD Work to be started has pipeline work proposed by Gail	

Sakra Hospital Road ORR (Devabeesnahalli) to Bellandur Kodi Road

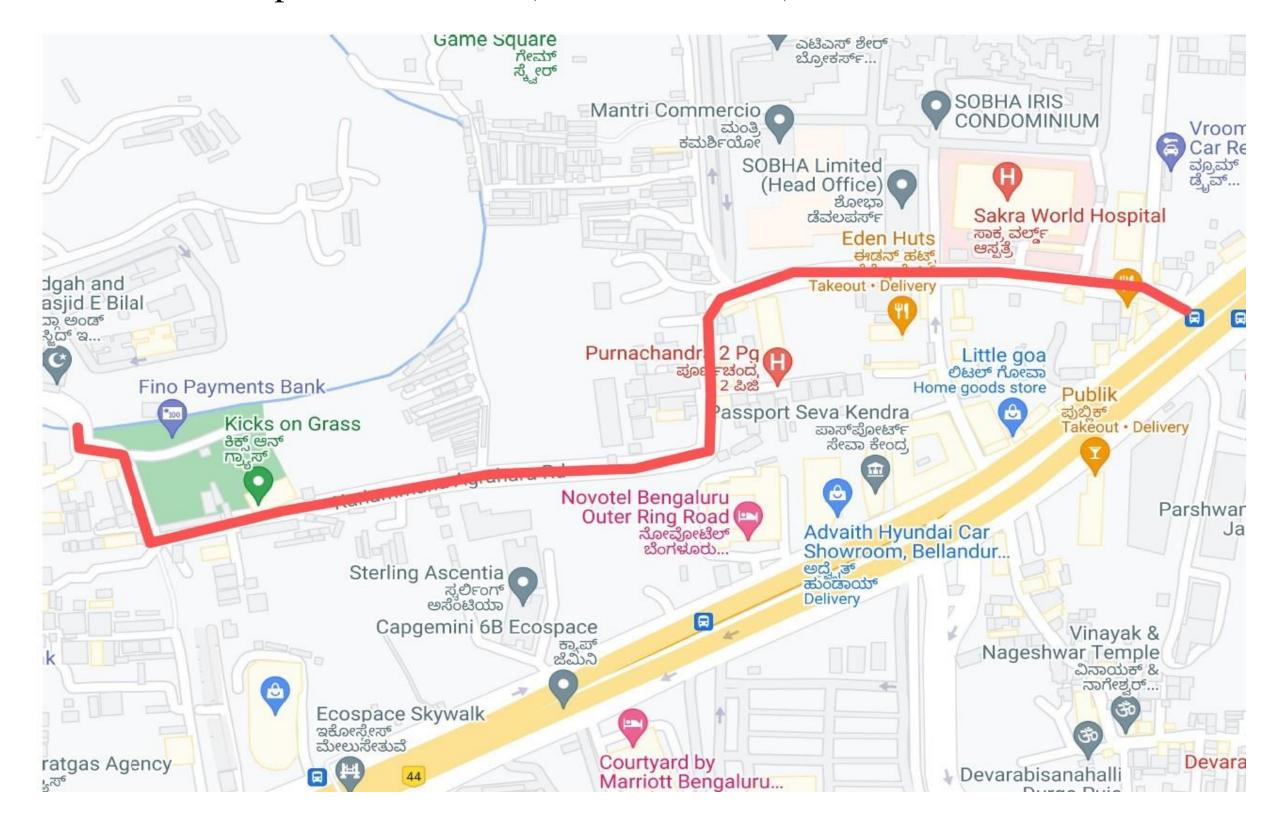



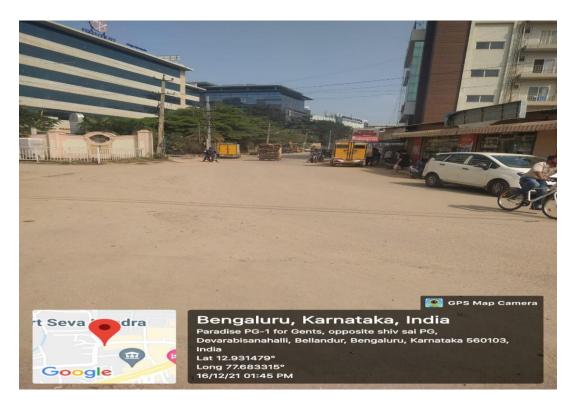







Road Name:		Croma 1	Croma Road		
From	ORR (Croma)	То	Balagere Road		
Length	1.80Km	Width	10Mtr		
Importance			This road is useful for Traffic flow from ORR to Panathur Balagere Connecting Road		
Present Status		_	Asphalted CompletedDrain work under progress		
On Going Works		> Drai:	> Drain work under progress		
Key Issues		> Heav Vent.	➤ Heavy Vehicles not passing through Railway Vent.		

Croma Road from ORR (Croma) to Balagere Road

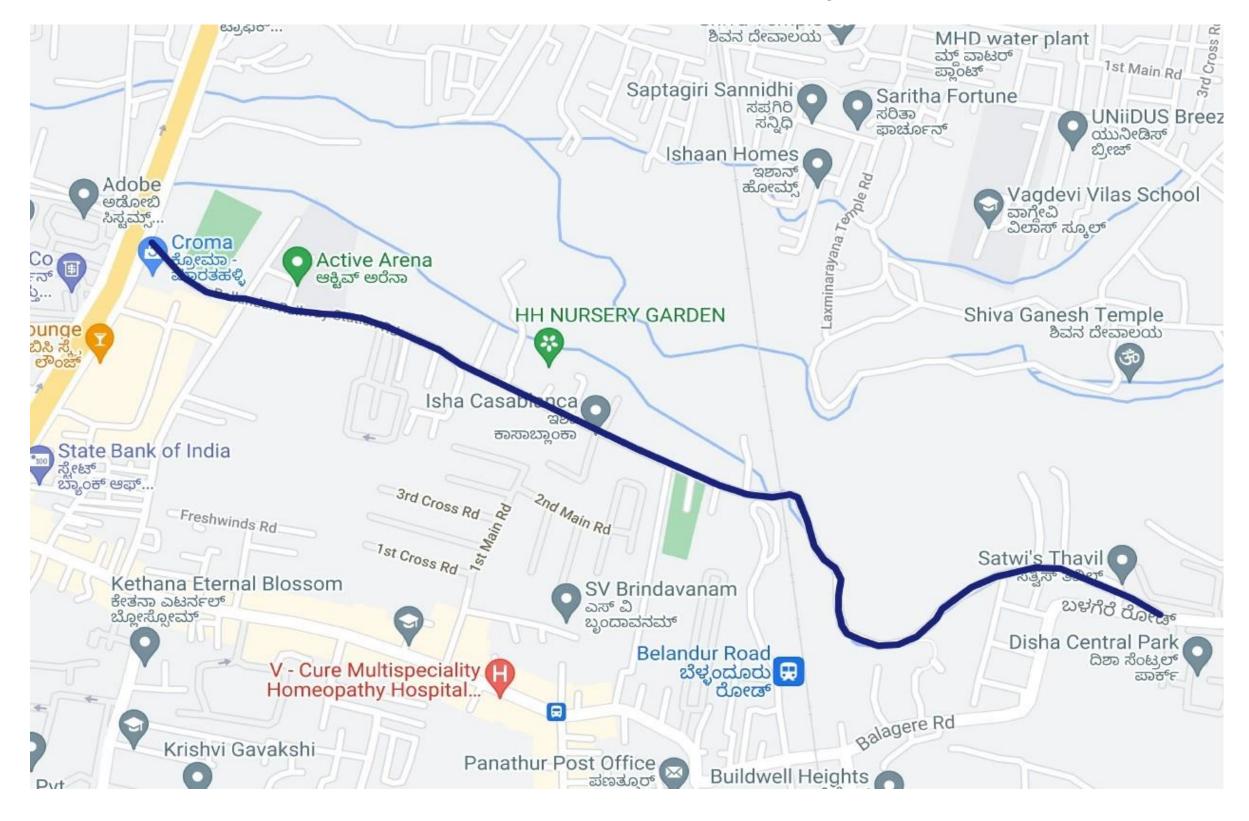


Road Name:		Gunjur Palya Road		
From	Panathur Balagere Road	То	Carmelaram Road & Varthur Gunjur Main Road	
Length	3.10Km	Width	9 To 12Mtrs	
Importance		This road is useful for Traffic flow from Panathur Balagere Main Road to Varthur Gunjur Main Road by avoiding traffic from Ibalur Junction to Kadubeesnahalli		
Present Status		➤ Motorable Condition work has been taken up in Escrow Grant		
Key Issues		 ➢ BESCOM UG Cable work under progress ➢ BWSSB Pipeline Work Under Progress ➢ Gail Gas pipeline work proposed by Gail India 		

Gunjur Palya Road from Panathur Balagere Road to Panathur Balagere Road

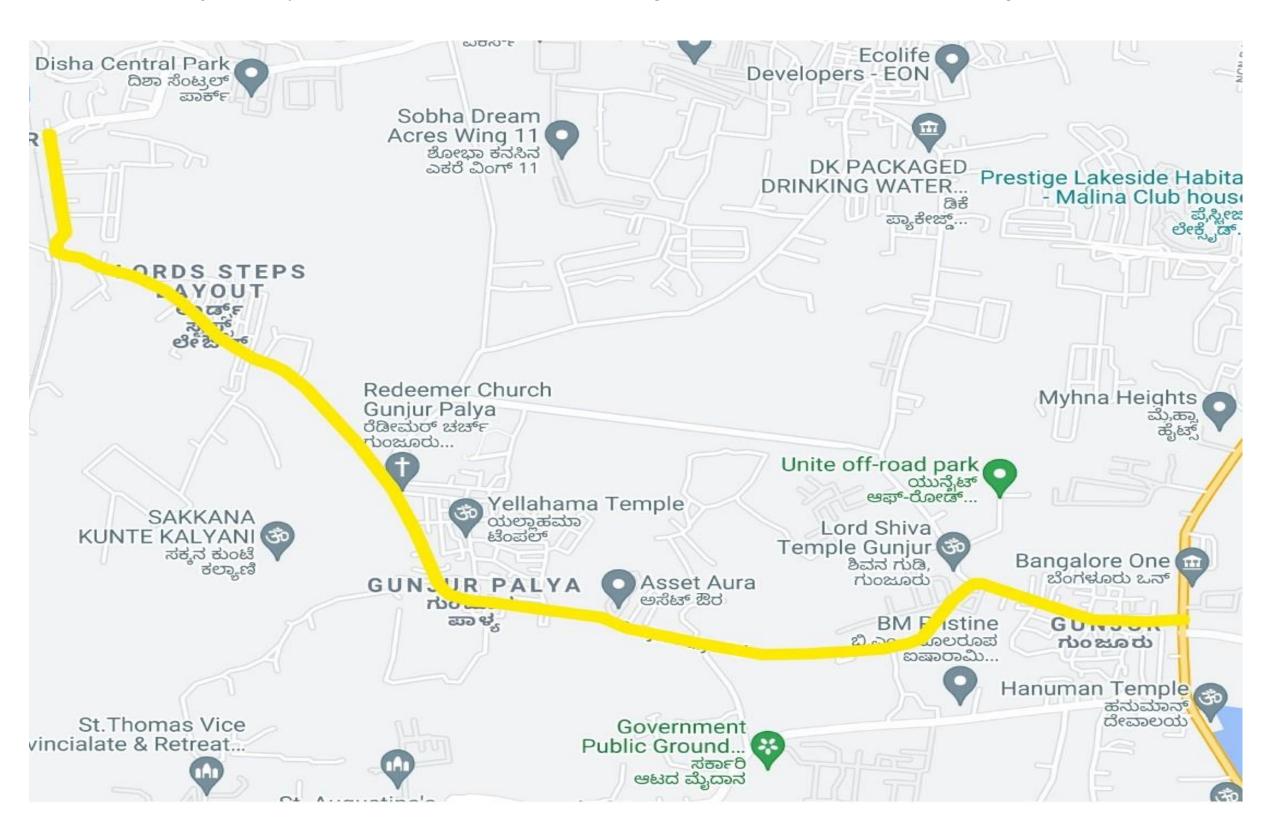


Road Name:		Carme	Carmelaram Road		
From	Sarjapura Road	То	Gunjur SH-35		
Length	4.50Km	Width	10 to 12Mtrs		
Importance		Sarjapu traffic	ad is useful for Traffic flow from ura Road to Gunjur SH-35 by avoiding from Iblur to Lowry Junction and also t HAL.		
Present Status		> Roa	➤ Road is in Good Condition & Motorable		
Key Issues			➤ BWSSB Cutting ➤BESCOM Cutting		

Carmelaram Road from Sarjapura Road to Gunjur SH-35

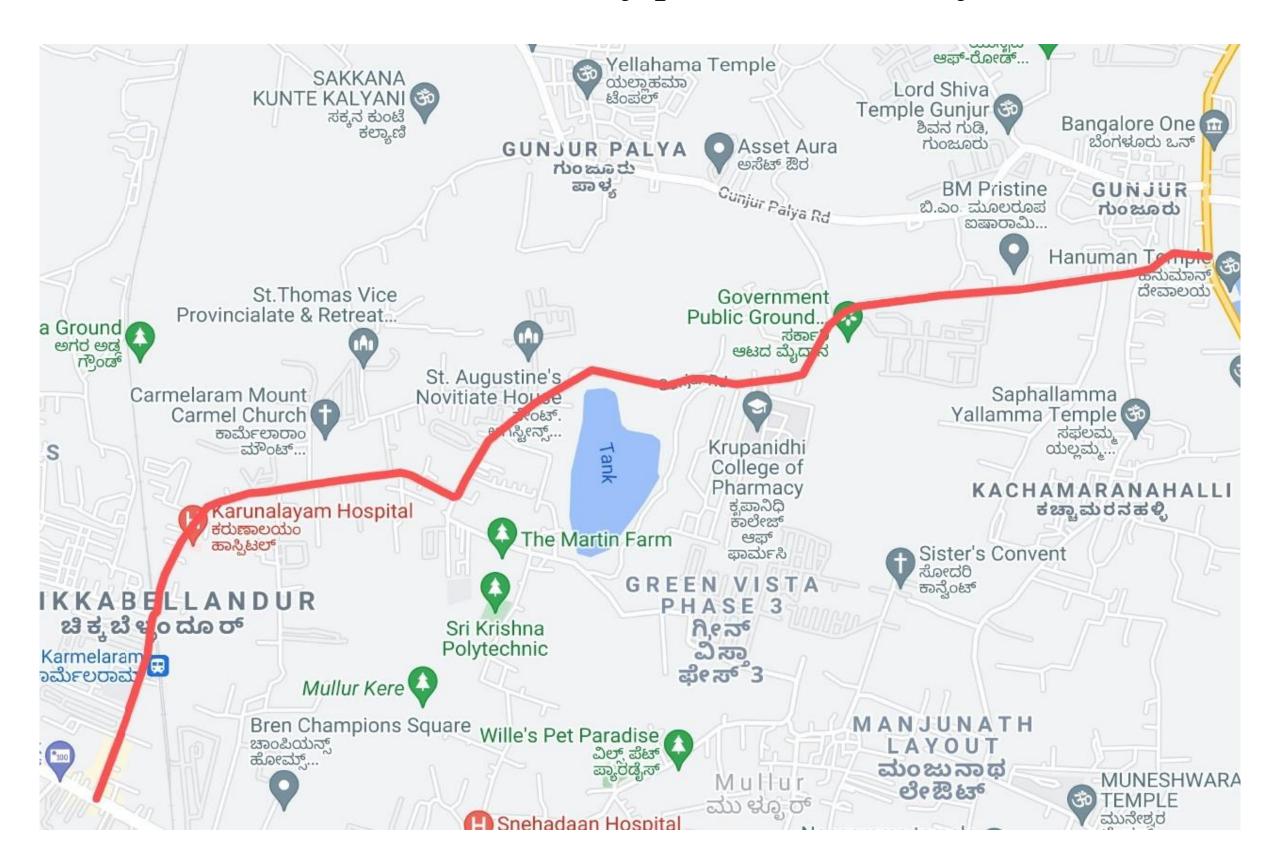


Road Name:		Old Air	Old Airport Road		
From	Surajandas Junction	То	Varthur Kodi		
Length	8.60Km	Width	24.00Mtrs		
Importance		Surajar	This road is useful for Traffic flow from Surajandas Junction to Varthur Kodi by avoiding traffic Marathahalli to Lowry Junction		
Present Status		> Roa	d is in Good Condition & Motorable		
On Going Works		> Und	➤ Underpass work at Kundalahalli Junction		
Key Issues		> BES	COM Work under progress		

Old Airport Road from Surajandas Junction to Varthur Kodi

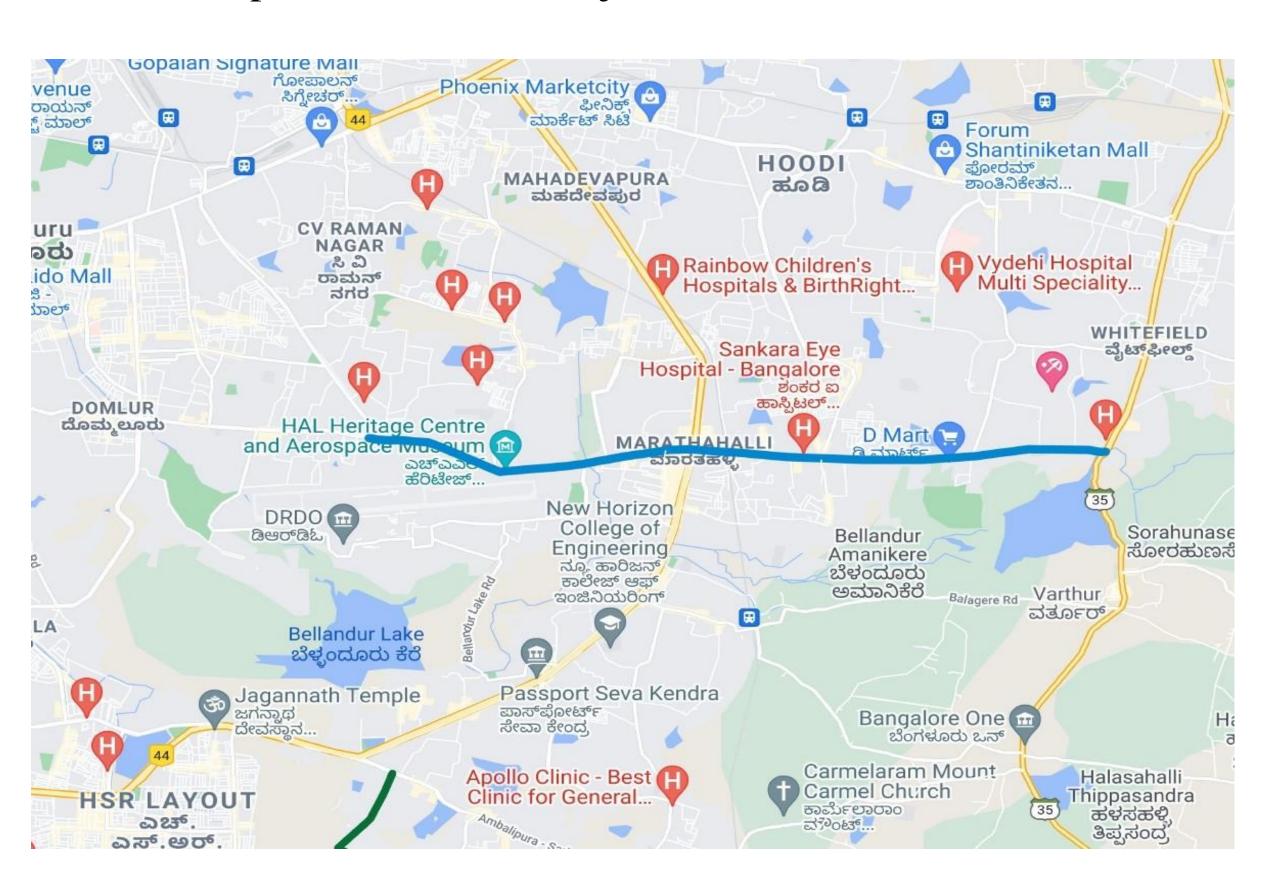


Road Name:		Varthur Gunjur Road (SH-35) (Handed over to KRDCL)		
From	Varthur Kodi	То	Gunjur	
Length	4.70Km	Width	12Mtrs	
Importance		This road is useful for Traffic flow from SH-35 at Gunjur to Hopefarm Junction by avoiding traffic from Iblur to Lowry Junction		
Present Status		> KR	> KRDCL Work Under Progress	

Varthur Gunjur Road (SH-35) (Handed over to KRDCL) from Varthur Kodi to Gunjur

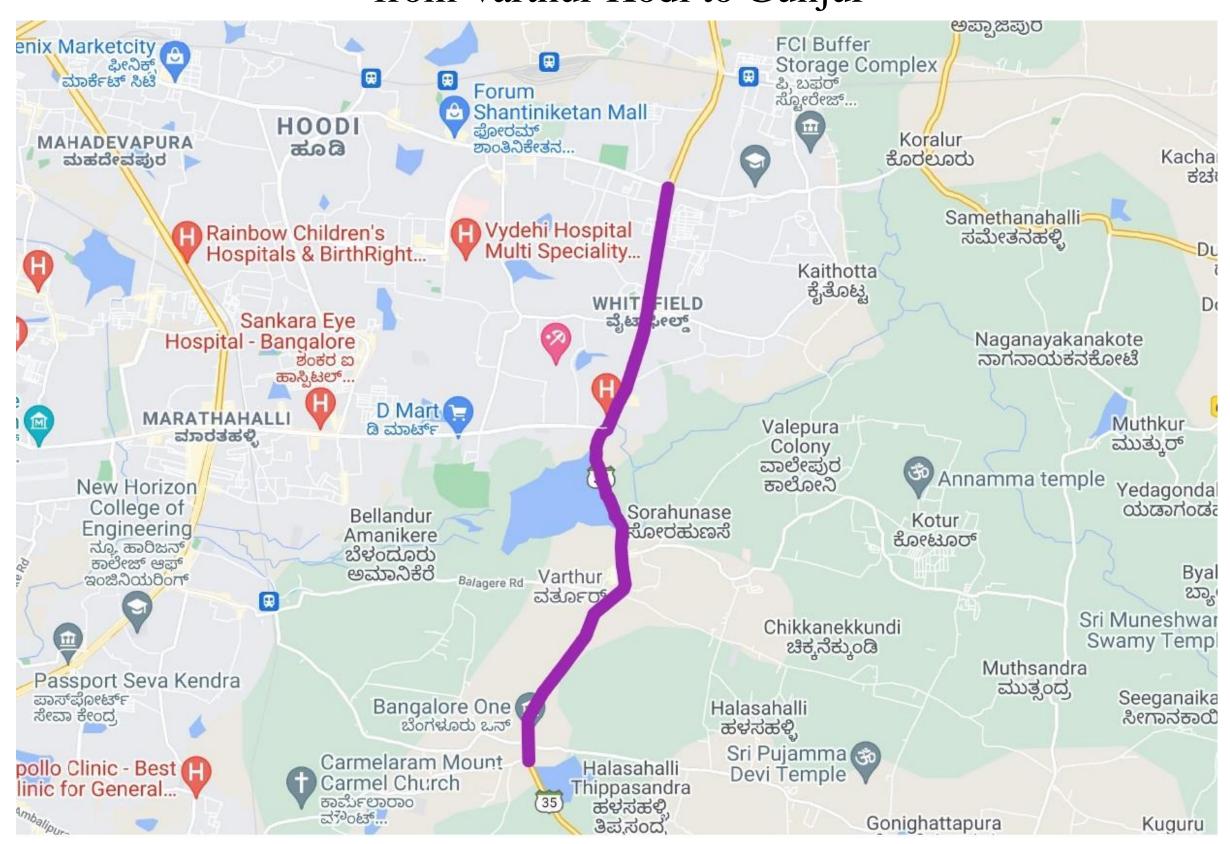


Road Name:		Doddanekundi Main Road		
From	ORR (ISRO Junction)	То	OAR	
Length	2.40Km	Width	8 to 10Mtrs	
Importance		This road is useful for Traffic flow from ORR (ISRO Junction) to OAR by avoiding traffic from Marathahalli to ISRO Junction		
Present Status		> Drain and Footpath Work under Progress		
On Going Works		➤ Asphalt Work to be Started		
Key Issues		➤ Applied BBMP Forest Department for Tree Cutting.		

Doddanekundi Main Road from ORR (ISRO Junction) to OAR

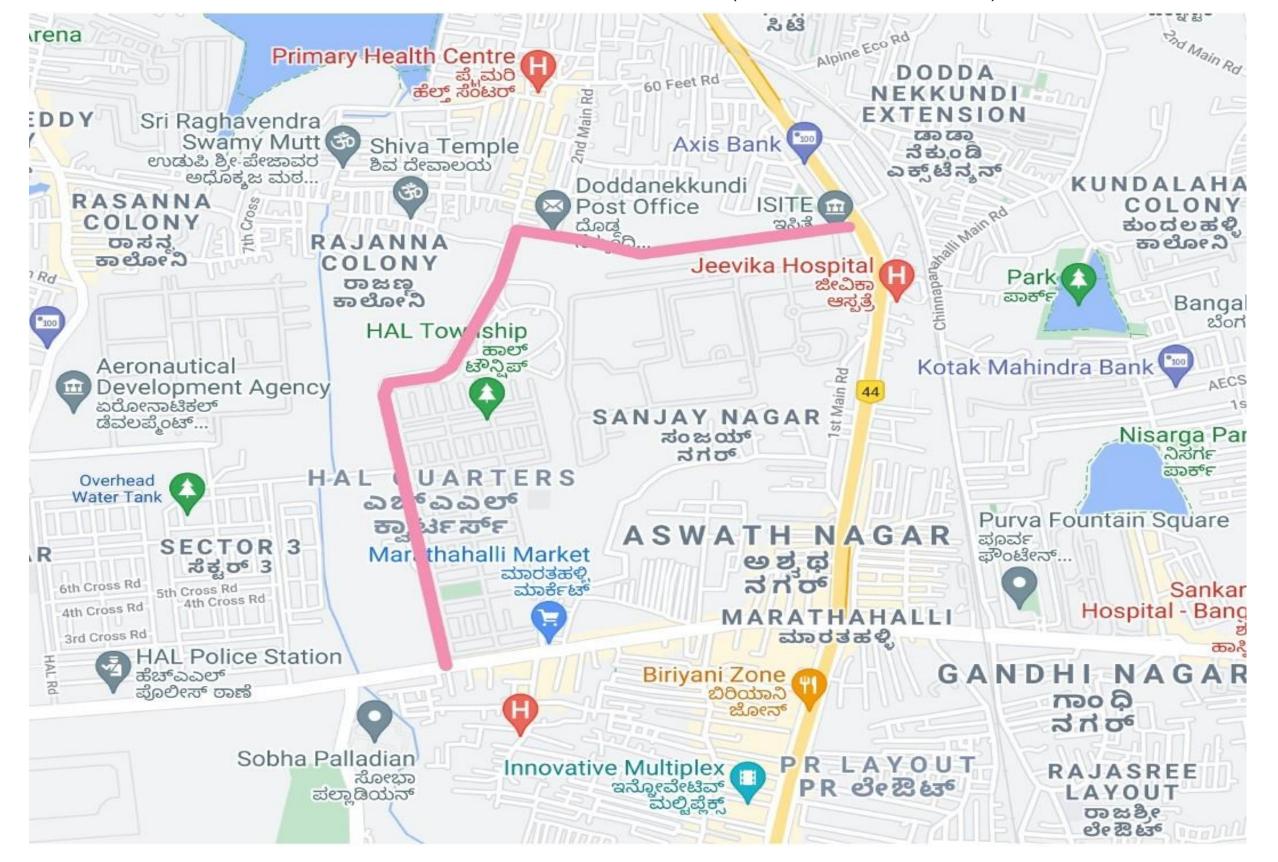



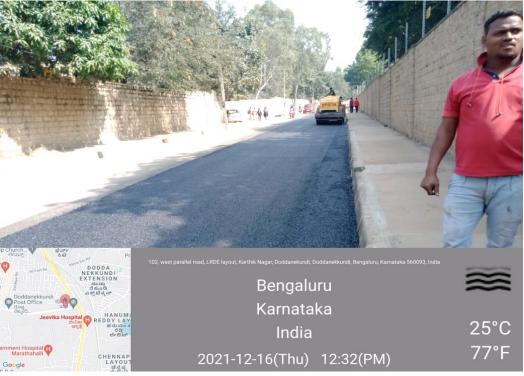






Road Name:		Doddanekundi Village Road		
From	ORR (Doddanekundi)	То	Doddanekundi Road	
Length	1.30Km	Width	9.00Mtrs	
Importance		This road is useful for Traffic flow from ORR to Doddanekundi Road by avoiding traffic from ISRO Junction to Doddanekundi Underpass		
Present Status		Drain Work under Progress		
On Going Works		➤ Asphalt Work to be Started		

Doddanekundi Village Road from ORR (Doddanekundi) to Doddanekundi Road

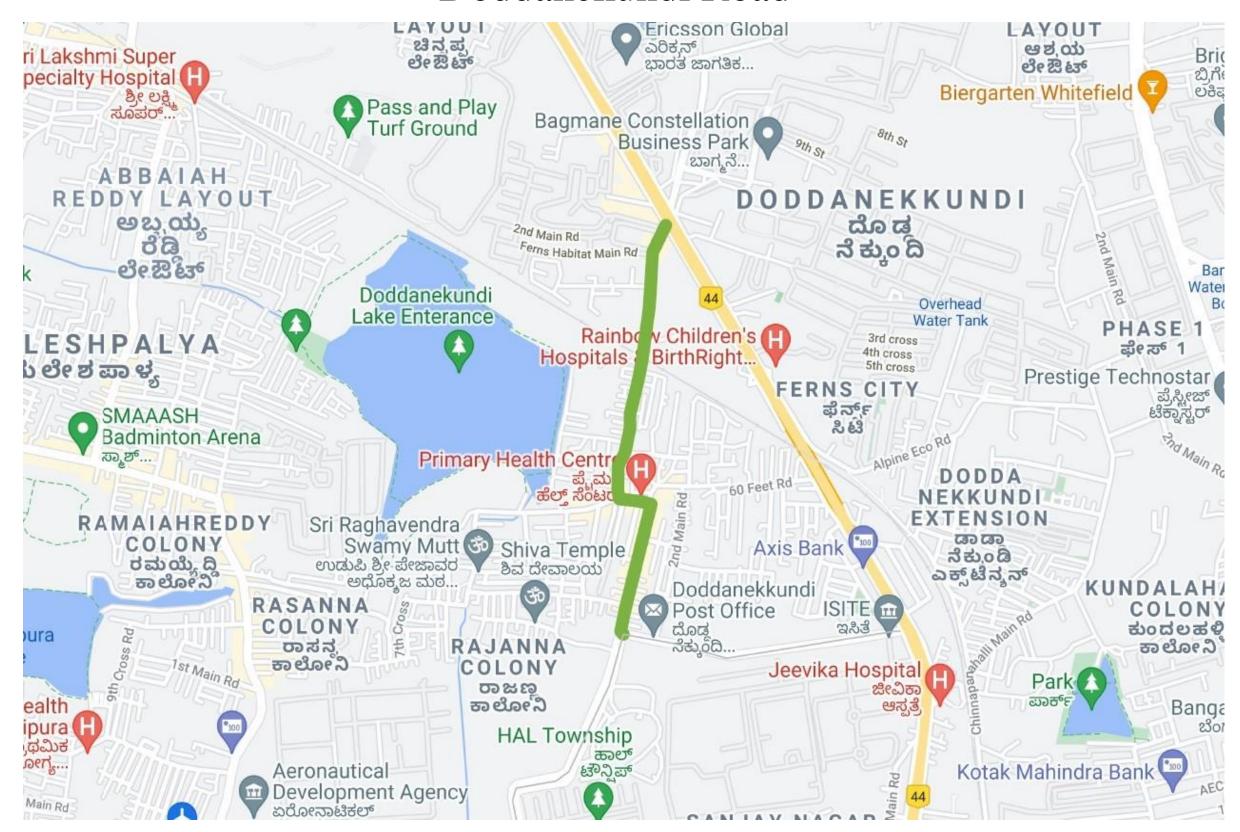










Road Name:		Graphit	Graphite India Road		
From	OAR Kundalahalli	То	Whitefield Road		
Length	4.80Km	Width	15 Mtrs		
Importance		OAR K Main R	This road is useful for Traffic flow from OAR Kundanahalli Junction to Whitefield Main Road by avoiding traffic from Marathahalli Junction to Lowry Junction		
Present Status		_	Drain work and Footpath Work under Progress		
On Going Works		> Drain Progres	n work and Footpath Work under s		
Key Issues			➤ BWSSB Cutting. ➤ BESCOM Cutting.		

Graphite India Road from OAR Kundalahalli to Whitefield Road

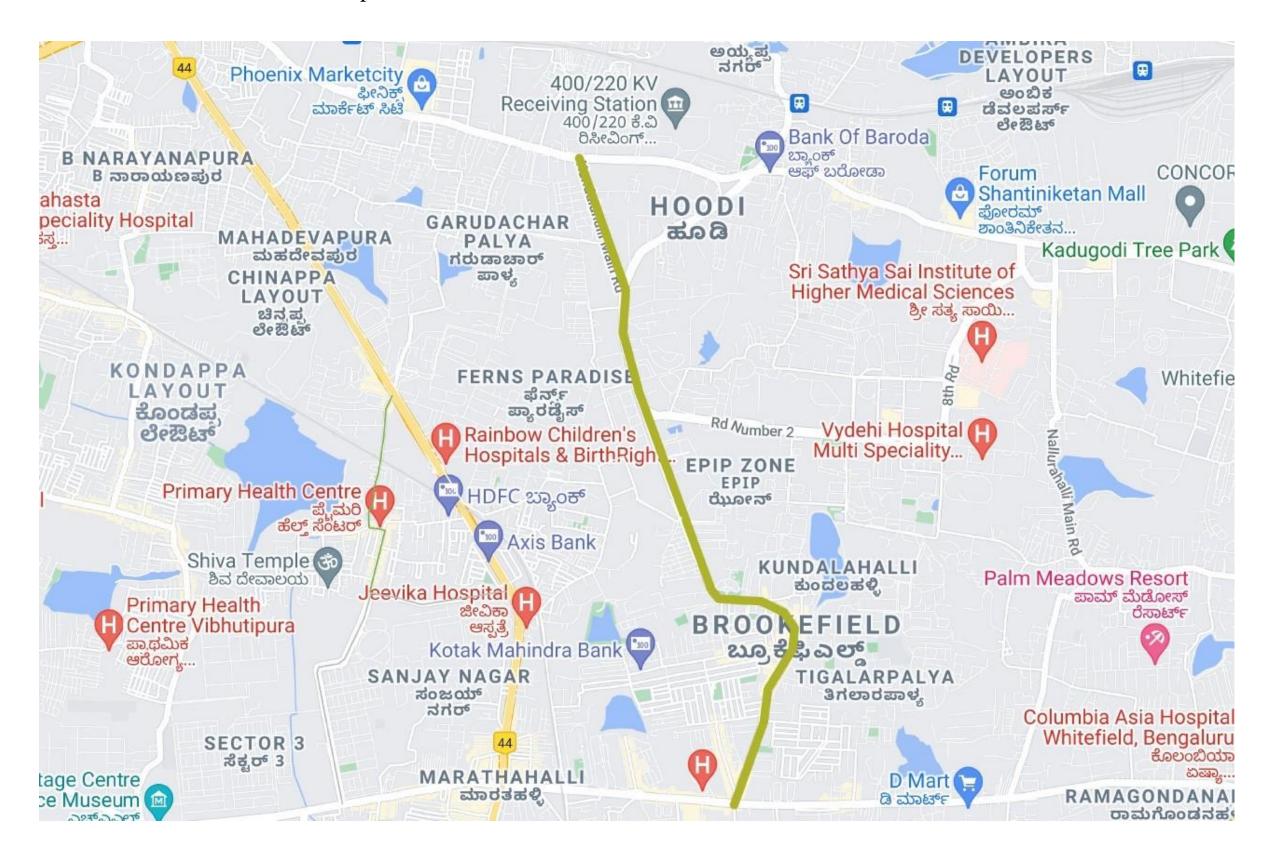









Road Name:		Alphine Echo Road		
From	ORR Rainbow hospital	То	Graphite India Road	
Length	2.30Km	Width	10 to 12Mtrs	
Importance		This road is useful for Traffic flow from ORR Rainbow hospital to Graphite India Road Road by avoiding traffic from Lowry Junction to ORR Rainbow hospital		
Present Status		Drain desilting Work under progress		

Alphine Echo Road from ORR Rainbow hospital to Graphite India Road

